Delivery 1 - Load 1 of 2 - Artic 13.6 m

10 pallets in 5 of 5 floor positions | 364 forms | tallest column 2522 mm of 2650 mm inside height

Column heights do not fall to the tail: unload order was kept, which the crew needs, and it conflicts with loading tallest-forward on this load.

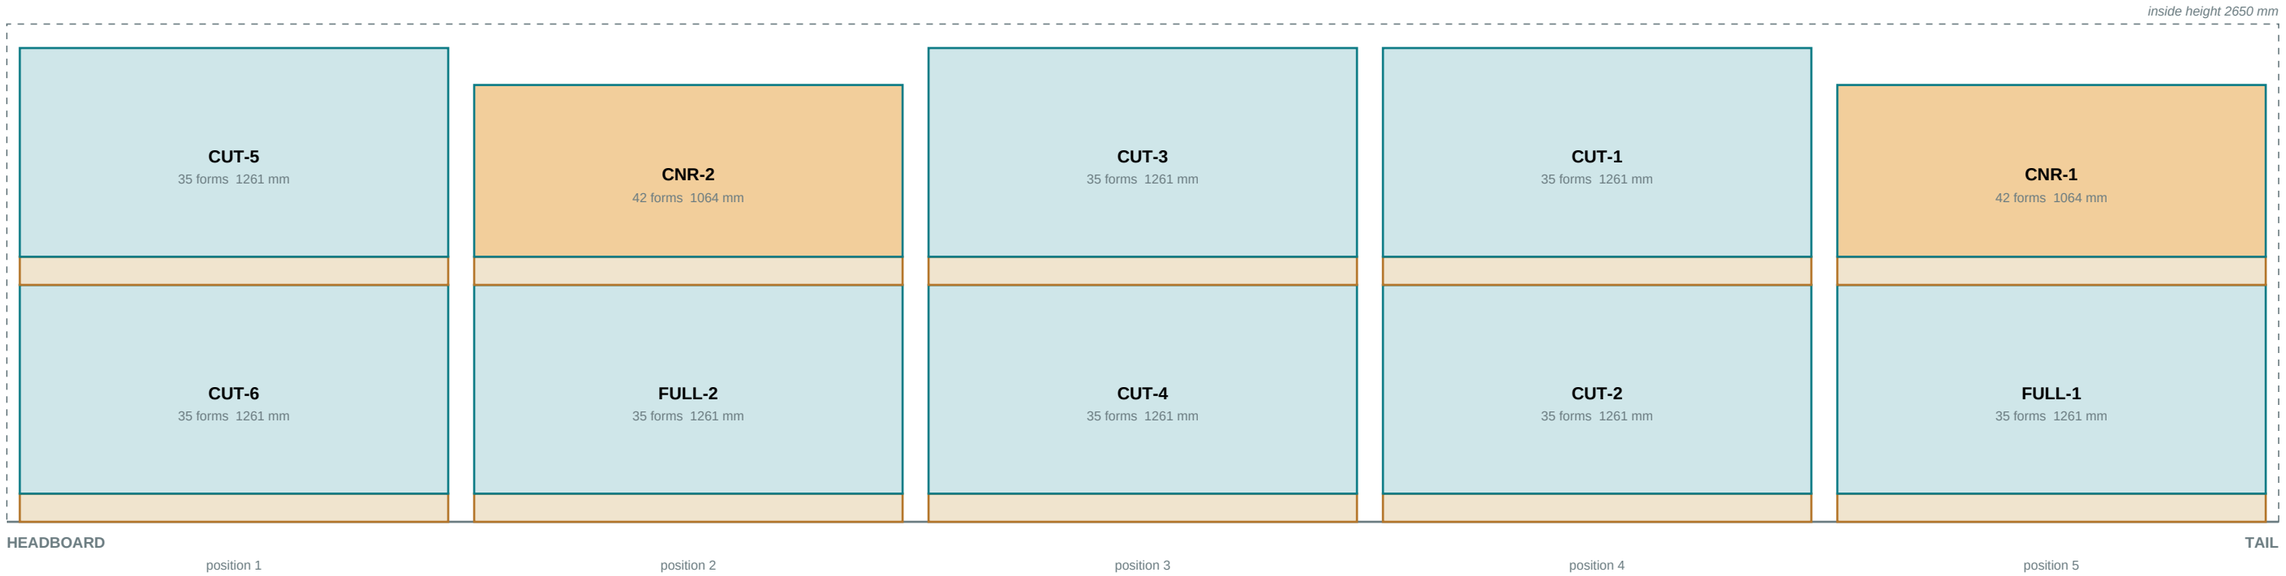

Unload order - 9 of 9 pallets come off out of build order, the price of stacking tallest forward

1. CNR-1 8in Std corners 42 forms courses L1 courses 1-3
2. FULL-1 8in Std straights 35 forms courses L1 courses 1-3
3. CUT-1 8in Std straights 35 forms courses L1 courses 1-8
4. CUT-2 8in Std straights 35 forms courses L1 courses 1-9
5. CUT-3 8in Std straights 35 forms courses L1 courses 2-9
6. CUT-4 8in Std straights 35 forms courses L1 courses 3-9
7. CNR-2 8in Std corners 42 forms courses L1 courses 4-6
8. FULL-2 8in Std straights 35 forms courses L1 courses 4-7
9. CUT-5 8in Std straights 35 forms courses L1 courses 4, 5, 6, 7, 9
10. CUT-6 8in Std straights 35 forms courses L1 courses 6-8

Nudura™ **WAGON STACKING PLAN** **D1 LOAD 1**

Tallest column at the headboard; last needed on the floor

PROJECT	ES26-086 Tremco CPG Poland - Villa Bosnia	FORMS	364
VEHICLE	Artic 13.6 m	POSITIONS	5 of 5
PALLETS	10	TALLEST	2522 mm

Delivery 1 - Load 2 of 2 - Artic 13.6 m

2 pallets in 1 of 5 floor positions | 23 forms | tallest column 916 mm of 2650 mm inside height

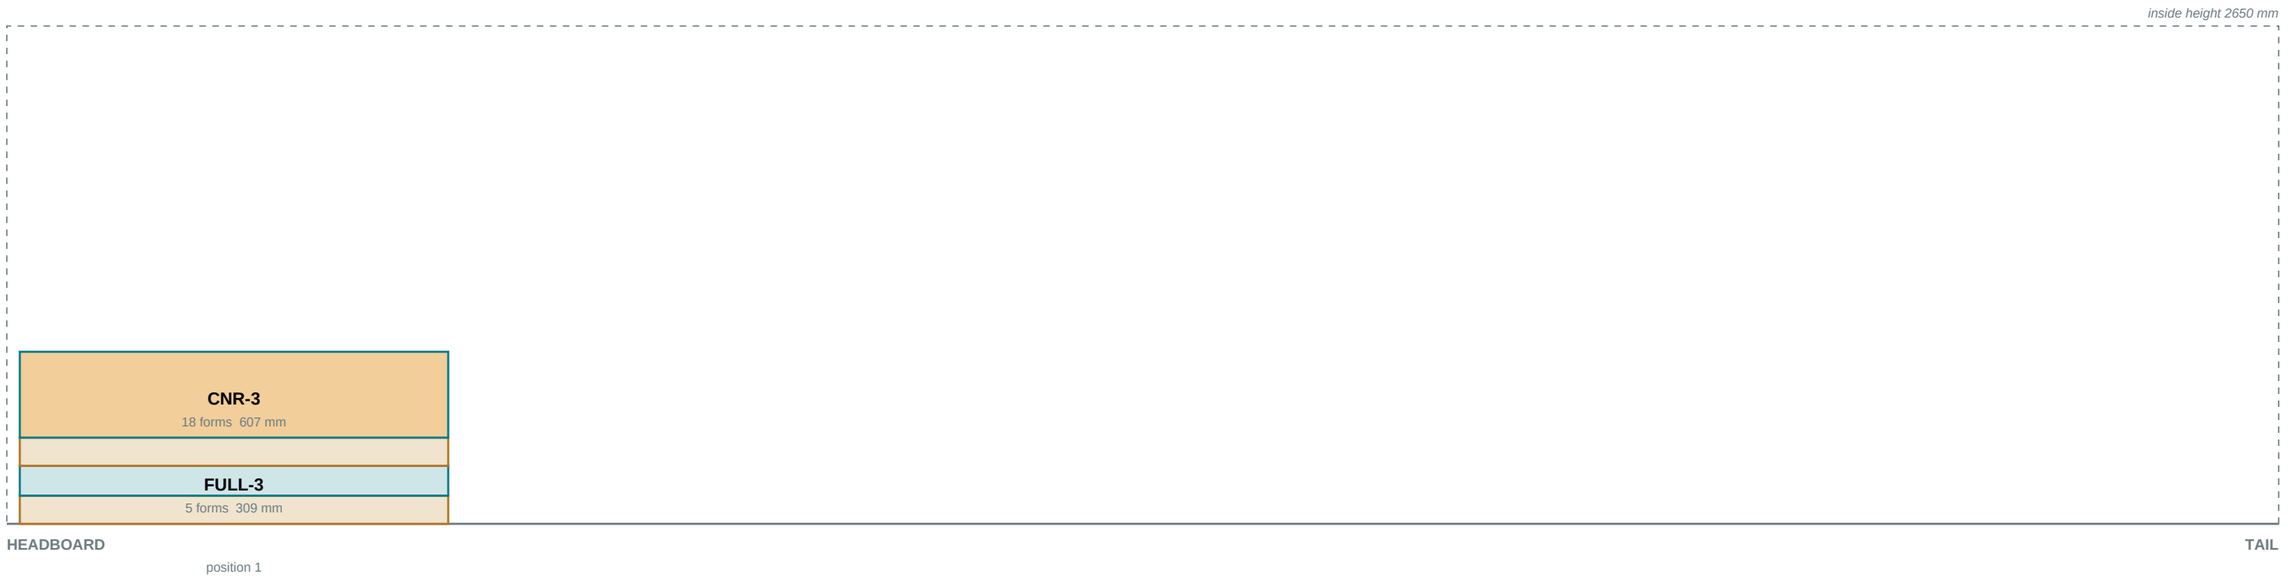

Unload order - 1 of 1 pallets come off out of build order, the price of stacking tallest forward

1. CNR-3 8in Std corners 18 forms courses L1 courses 7-9
2. FULL-3 8in Std straights 5 forms courses L1 courses 8-9

Nudura™ **WAGON STACKING PLAN** **D1 LOAD 2**

Tallest column at the headboard; last needed on the floor

PROJECT	ES26-086 Tremco CPG Poland - Villa Bosnia	FORMS	23
VEHICLE	Artic 13.6 m	POSITIONS	1 of 5
PALLETS	2	TALLEST	916 mm

Delivery 2 - Load 1 of 1 - Artic 13.6 m

9 pallets in 5 of 5 floor positions | 285 forms | tallest column 2522 mm of 2650 mm inside height

Column heights do not fall to the tail: unload order was kept, which the crew needs, and it conflicts with loading tallest-forward on this load.

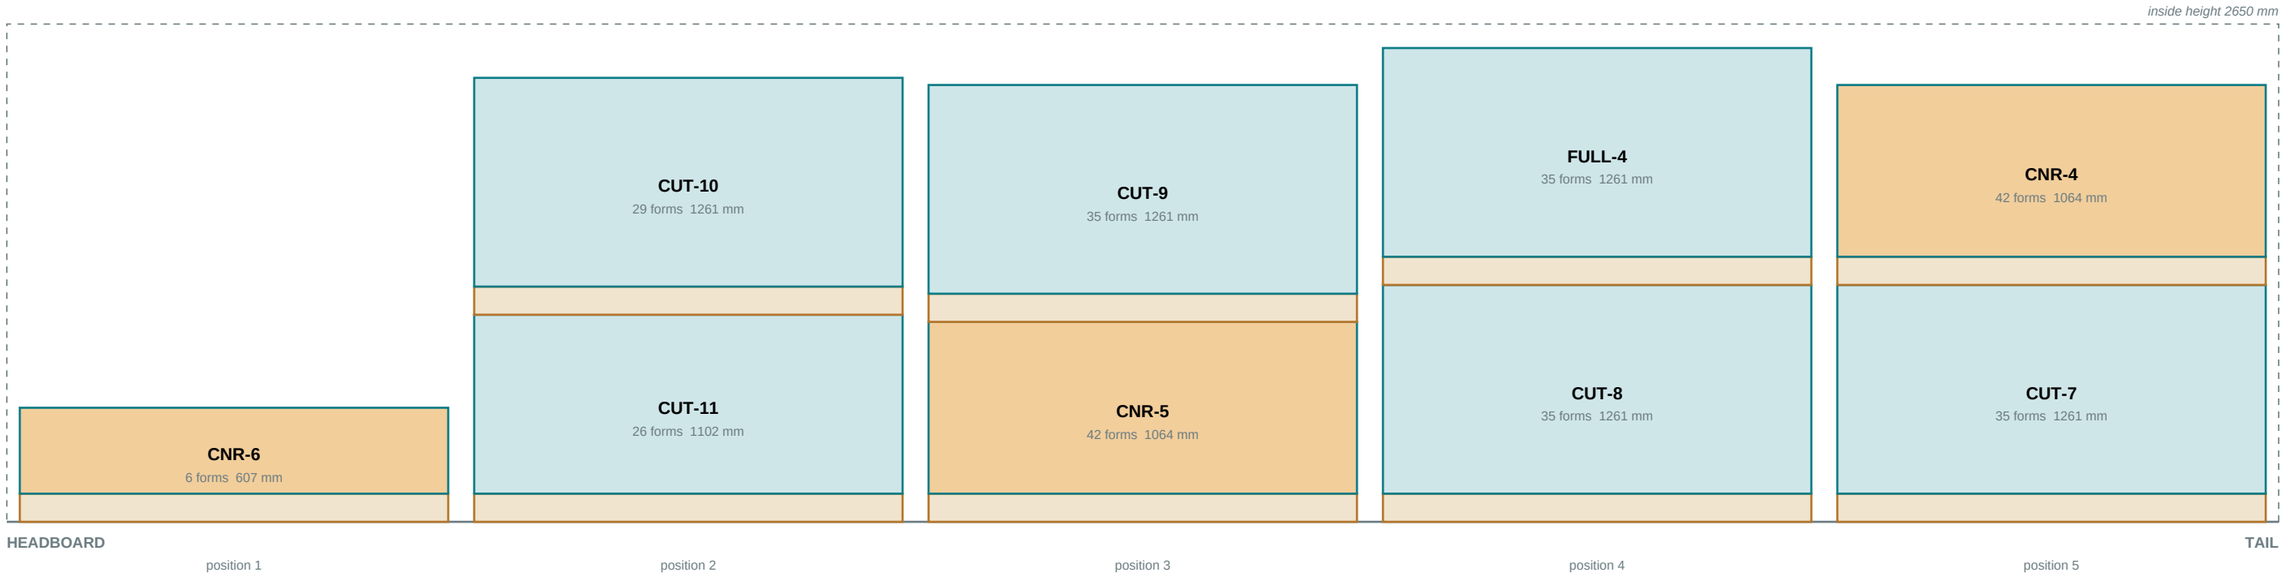

Unload order - 8 of 8 pallets come off out of build order, the price of stacking tallest forward

1. CNR-4 8in Std corners 42 forms courses L2 courses 1-4
2. CUT-7 8in Std straights 35 forms courses L2 courses 1-7
3. FULL-4 8in Std straights 35 forms courses L2 courses 1-7
4. CUT-8 8in Std straights 35 forms courses L2 courses 2-7
5. CUT-9 8in Std straights 35 forms courses L2 courses 3-7
6. CNR-5 8in Std corners 42 forms courses L2 courses 4-8
7. CUT-10 8in Std straights 29 forms courses L2 courses 4-8
8. CUT-11 8in Std straights 26 forms courses L2 courses 7-8
9. CNR-6 8in Std corners 6 forms courses L2 course 8

Nudura™ **WAGON STACKING PLAN** **D2 LOAD 1**

Tallest column at the headboard; last needed on the floor

PROJECT	ES26-086 Tremco CPG Poland - Villa Bosnia	FORMS	285
VEHICLE	Artic 13.6 m	POSITIONS	5 of 5
PALLETS	9	TALLEST	2522 mm
